

**VIAVI**

**Cable Id :**  
**Location A :** LOC A  
**Job Id :**

**Fiber Id :** Fiber 3166  
**Location B :** LOC B  
**Technician Id :**

SmartOTDR (S/N 28162)

E100AS (S/N 28162)

Date : 21/12/2025 15:20

Test Setup

OTDR EXPERT

1310nm

30ns

5km

64cm

20.0s

1.46750(G652 G657)

-79.0 dB

Alarms

Thresholds

None

Summary

Filename  
24 05 no amroula gp keshlar gp.sor

Laser nm  
1310

Link Loss dB  
2.590

Link Orl dB  
41.59


Fiber End Km  
2.453

Direction  
LOC A > LOC B

Event  
6

Alarms

OTDR 1310nm

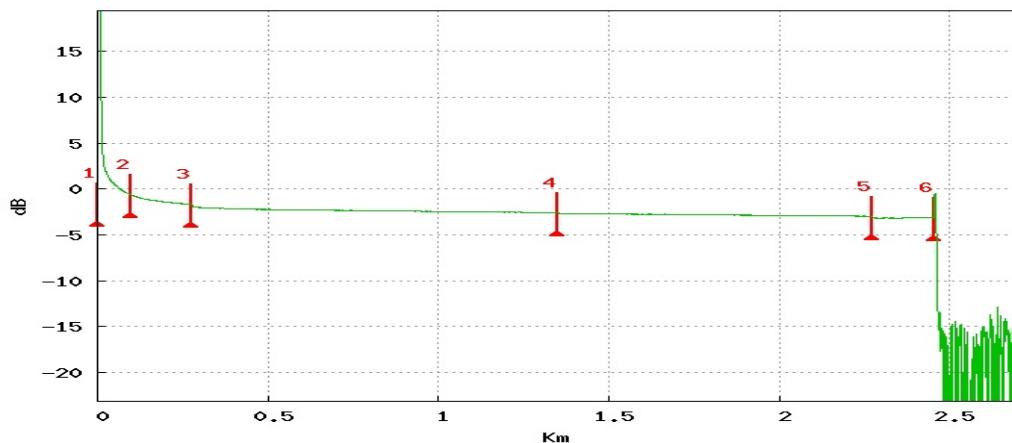

Event	Distance	Loss	Reflect.	Slope	Section	T. Loss
	Km	dB	dB	dB/km	Km	dB
1	0.000	0.551	>-19.27		0.000	0.000
2	0.096	0.484			0.096	0.032
3	0.275	0.463			0.179	1.092
4	1.351	0.063		0.471	1.076	2.061
5	2.271	0.195		0.321	0.920	2.419
6	2.453		-59.24		0.181	2.590
